



ICAM Technical Project Plan

July 24, 2026

ICAM Technical Project Plan

Submitted To:

Submitted By:

*General Dynamics Information Technology, Inc.
3150 Fairview Park Drive
Suite 100
Falls Church, VA 22042-4504
(703) 995-8700
<http://www.gdit.com>
DUNS Number: 067641597
CAGE Code: 07MU1
Business Size Status for the North American Industry
Classification System (NAICS) code: Large*

POC:

*Randy Mears
(256) 947-5032
randy.mears@gdit.com*

Disclosure Statement:

This proposal includes data that shall not be disclosed outside the Government and shall not be duplicated, used, or disclosed—in whole or in part—for any purpose other than to evaluate this proposal. If, however, a contract is awarded to this offeror as a result of—or in connection with—the submission of this data, the Government shall have the right to duplicate, use, or disclose the data to the extent provided in the resulting contract. This restriction does not limit the Government's right to use information contained in this data if it is obtained from another source without restriction. The data subject to the restriction are contained in sheets with the following legend: "Use or disclosure of data contained on this sheet is subject to the restriction on the title page of this proposal."

Table of Contents

1.0	Background & Understanding of the Requirement	1
2.0	TECHNICAL VOLUME & APPROACH	1
2.1	Phase 1	1
2.2	Phase 2:	1
2.2.1	Collecting roles and entitlement data	1
2.3	SYSTEM ARCHITECTURE	2
2.4	QUALITY ASSURANCE	3
2.5	SECURITY & COMPLIANCE	3
3.0	PROGRAM MANAGEMENT	4
4.0	STAFFING PLAN	4
4.1	Phase 1	4
4.2	Phase 2	4
5.0	SCHEDULE & MILESTONES	5
5.1	Phase 1	5
5.2	Phase 2 – Achieving 50,000 application throughput	5
6.0	RISK MANAGEMENT	5

List of Figures

Figure 1. GDIT’s Vast Corporate Experience	1
--	---

List of Tables

Table 1. GDIT Digital Accelerators	3
Table 2. GDIT’s Assessment of Executing Both, User and Program Mission Projects	8
Table 3. Recommended Changes to the Draft DD254	15

1.0 Background & Understanding of the Requirement

Goal: 150 applications onboarded per month

Phase 1: Rapid onboarding of 250 – 300 applications to DOD E-ICAM Identify Provider(IDP) and Automated Account Provisioning (AAP)

One of the bottlenecks and pain points during the onboarding process is familiarizing each Mission Partner with the roles & responsibilities. While onboarding guides exist, many mission partners have follow up questions. The only effective channel to answer these questions remain the ICAM onboarding team.

GDIT's Phase 1 enabler is to provide an alternative channel to allow mission partners to chat with an AI assistant for their level 100 and level 200 about the onboarding guide. This channel, which we are naming as an AI concierge bot, will increase the mission partner satisfaction by obtaining accurate responses quickly.

Pain point/ bottleneck	Potential Solution	
Meeting planner and scheduling is a pain (2 nd or third tier priority)		
Mission Partners struggle to fill out roles in a correct manner – ICAM team will send a link to the MP with the sharepoint		
Having a lot of meetings with mission partners – almost a daily calls	Q&A website for public	
MP have a hard time interfacing Sailpoint APIs – error message troubleshooting		
Mission Partner Familiarization		

Phase 2: Scaling to 50k+ applications

2.0 TECHNICAL VOLUME & APPROACH

2.1 Phase 1

2.2 Phase 2:

2.2.1 Collecting roles and entitlement data

Onboarding one role onto ICAM requires 34 fields of information to be identified. This includes basic information on the role, such as the name & description, attributes for dynamic approval, and intra SOD conflict policies.

Some small application may have less than a dozen roles; other larger applications may have hundreds. Furthermore, roles and their policies are often dynamic and changing.

This section focuses on supporting application owners by providing two complementary channels for efficiently collecting role and entitlement data.

Channel 1 enhances the existing Self-Service Onboarding Portal with intelligent tooling and agentic workflows that reduce the manual burden of collecting and validating information.

Channel 2, which is targeted for complex applications, provides a downloadable data collection toolkit that application owners can integrate with their existing code repository and CI/CD pipelines to capture entitlement information directly from the source.

The features, benefits and outcomes of both channels are listed below.

Channel 1: Improvements to the Self-Serve Onboarding Portal (DEAS Admin Portal)

Feature	Benefit	Outcome
AI Concierge Bot	Reduce cognitive burden of having to manually populate the self-Serve Onboarding Portal (DEAS Admin Portal)	Improve quality and accuracy of responses by 15%
Agentic Role Parser – Role Mining	Allows application owners to copy and paste role information in the formats they prefer	Reduces data collection time by 50% automatically structuring the unstructured data
Agentic Role Parser – SCIM API Translator	Applications with predefined SCIM 2.0 standards can be queried efficiently	Leverage existing standards to maintain accuracy of existing defined roles
Agentic Role Parser – Spreadsheet & ATO Document Ingestion	Process existing access matrices and ATO packages that application developers have already maintained	Reduce duplicative data collection efforts by leveraging existing ATO documents

Channel 2: ICAM Onboarding Software for App Owners

Large application owners Performs static code analysis, readme documentation, configuration file parsing, API scanning and OAuth metadata searches to identify roles and descriptions.

Dependency is that pipelines have access to Government

Feature	Benefit	Outcome
Self-deployable Role Discovery Toolkit: designed to search application repositories and documentation	Automated extraction pulls up to hundreds of roles directly from the code repository and sources of truth	50% improvement in accuracy, 50% improvement in data collection


Feature	Benefit	Outcome
Toolkit with CI/CD Pipeline Hooks	Reduces onboarding administrative burden for applications that expect to have many changing roles	Ensures maximum consistency on role adds and role deletions, with auditability

2.3 SYSTEM ARCHITECTURE

Phase 1:

Phase 2:

GDIT prefers to leverage Azure Serverless services that are deployable in IL5

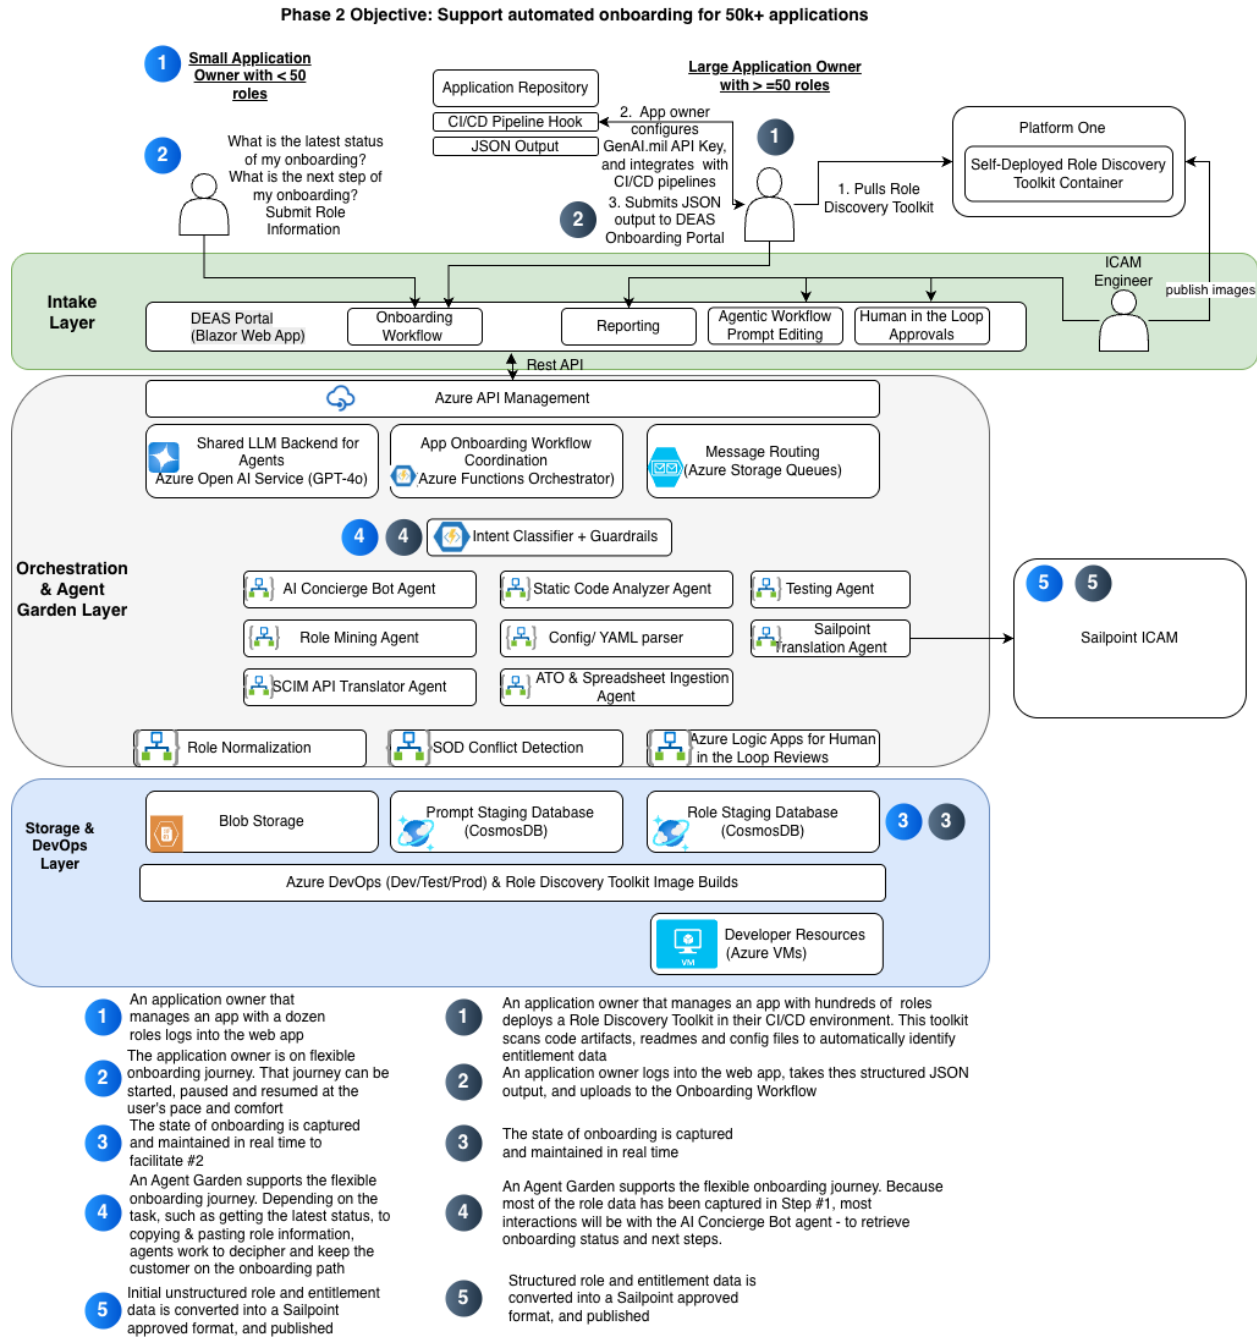

2.4 QUALITY ASSURANCE

Testing

2.5 SECURITY & COMPLIANCE

The ICAM Onboarding Application leverages a defense-in-depth approach to address infrastructure security, identity and access government, application-layer controls, continuous monitoring and agentic layer risks.

All platform services leverage Azure serverless services, eliminating persistent attack surfaces, reducing the OS and runtime patch burden, and enabling native integration with Azure Key Vault, Managed Identity, and Azure Monitor for end-to-end IL5-compliant security controls.

Each of the AI agents runs under a discrete Azure Managed Identity with least-privilege permissions scoped to the resources it requires. An intent classifier acts as a routing mechanism to evaluate every single incoming LLM request; requests that are too broad, unknown or likely to contain prompt injections, are discarded before reaching an agent. Input guardrails further ensure no PII is evaluated while blocking attempts to override agent instructions. All agent activity, including LLM calls and orchestration decisions, are written to Azure Monitor logs providing a full audit trail.

3.0 PROGRAM MANAGEMENT

GDIT recommends a single prioritized backlog managed by a Product Owner. Work is organized into two week sprints, each producing working software improvements that DISA stakeholders can review and provide feedback on directly.

Daily standups keep cross-discipline dependencies between cloud infrastructure, AI, data and UI engineers visible and resolved before they become blockers.

GDIT recommends monthly milestone reviews tied to reviewing metrics including onboarding process time. This provides DISA a recurring touchpoint to assess improvement and align on next months tasks to improve onboarding velocity.

Progress is tracked in an Azure DevOps board, complete with sprint burndown, cumulative onboarding process time reduction, and defect trends. This cadence delivers the transparency and adaptability to keep the team focused on delivery a platform that onboards a variety of applications faster with every successive sprint.

4.0 STAFFING PLAN

4.1 Phase 1

4.2 Phase 2

Labor Category	Quantity	Description
Program/Product Manager	1	Overall feature prioritization, backlog management, stakeholder
Cloud Infrastructure Architects	1 Senior, 1 Junior	Supports the buildout of services in infrastructure as code
AI/ML Engineer	1 Senior, 1 Junior	Responsible for Agentic Workflow buildout and overall accuracy of responses
DevSecOps	1 Senior	~40% reduction in revision cycles
Data Engineer	1 Senior	Configuration of data model, data interfaces, databases and storage

Labor Category	Quantity	Description
Cybersecurity Engineer	1 Senior	Supports ATO documentation, cyber hardening, AI Risk Management
User Interface/User Experience Engineers	1 Senior, 1 Junior	Customer Facing Application Development including front end components and backend API creation
ICAM SMEs	2 Senior	Provide Voice of the Customer input through feature prioritization, testing and validation

5.0 SCHEDULE & MILESTONES

5.1 Phase 1

5.2 Phase 2 – Achieving 50,000 application throughput

Milestone	Target	Outcome
P2 M1:Phase 2 MPV live	Month 6	Baseline infrastructure and AI Concierge Workflows established
P2 M2: Role Data Collection Agents Deployed	Month 12	50% reduction in manual role data collection time
P2 M3: Channel 2 Toolkit Published (Zero Touch Discovery)	Month 24	~70% reduction for complex applications
P2 M4 :SoD & Normalization Reduce Rework	Month 24	~40% reduction in revision cycles
P2 M5: AI Tuning & Scale Optimization	Month 36	Full-cycle onboarding time optimized for 50k+ app onboarding workflows with 99.9% system uptime. Zero touch onboarding achieved for 80% of simple applications.

6.0 RISK MANAGEMENT
